



[www.habitatventures.com](http://www.habitatventures.com)

**Project Progress  
Status Update as on  
January 2023**

# Habitat Aura

PRM/KA/RERA/1251/310/PR/181219/002235  
Visit <https://rera.karnataka.gov.in> for further details.

AT SY. NOs. 49/1, 49/2 & 50 & 52/3, AREKERE VILLAGE  
BEGUR HOBLI, BANGALORE SOUTH TALUK

# WORK PROGRESS STATUS



## Tower – I (South)

### KEY ACTIVITIES

- Up to 17th Floor slab concreting 100% completed and 18<sup>th</sup> floor slab reinforcement works are in progress.
- Up to 11<sup>th</sup> floor block masonry works are 100% completed.
- 12th floor block masonry works are in progress.
- Up to 7th floor Internal plastering works are completed.
- 8<sup>th</sup> & 9<sup>th</sup> floor Internal plastering works are in progress.
- External plastering works 1<sup>st</sup>-10<sup>th</sup> floor are in progress.
- Up to 9<sup>th</sup> floor electrical wall conduiting and GI box fixing works are completed.
- 10<sup>th</sup> & 11<sup>th</sup> floor electrical wall conduiting and GI box fixing works are in progress.

# WORK PROGRESS STATUS



## Tower - II (North)

### KEY ACTIVITIES

- Up to 17th Floor slab concreting 100% completed and 18<sup>th</sup> floor shuttering works are in progress.
- Up to 11<sup>th</sup> floor block masonry works are 100% completed.
- 12th floor block masonry works are in progress.
- Up to 7th floor Internal plastering works are completed.
- 8<sup>th</sup> & 9<sup>th</sup> floor Internal plastering works are in progress.
- External plastering works 1<sup>st</sup>-10<sup>th</sup> floor are in progress.
- Up to 9<sup>th</sup> floor electrical wall pipe conduiting and GI box fixing works are completed.
- 10<sup>th</sup> & 11<sup>th</sup> floor electrical wall pipe conduiting and GI box fixing works are in progress.




TOWER-01 & 02 VIEW FROM WEST FACE



TOWER-01 & 02 VIEW FROM SOUTH WEST FACE



TOWER-01 & 02 VIEW FROM SOUTH FACE

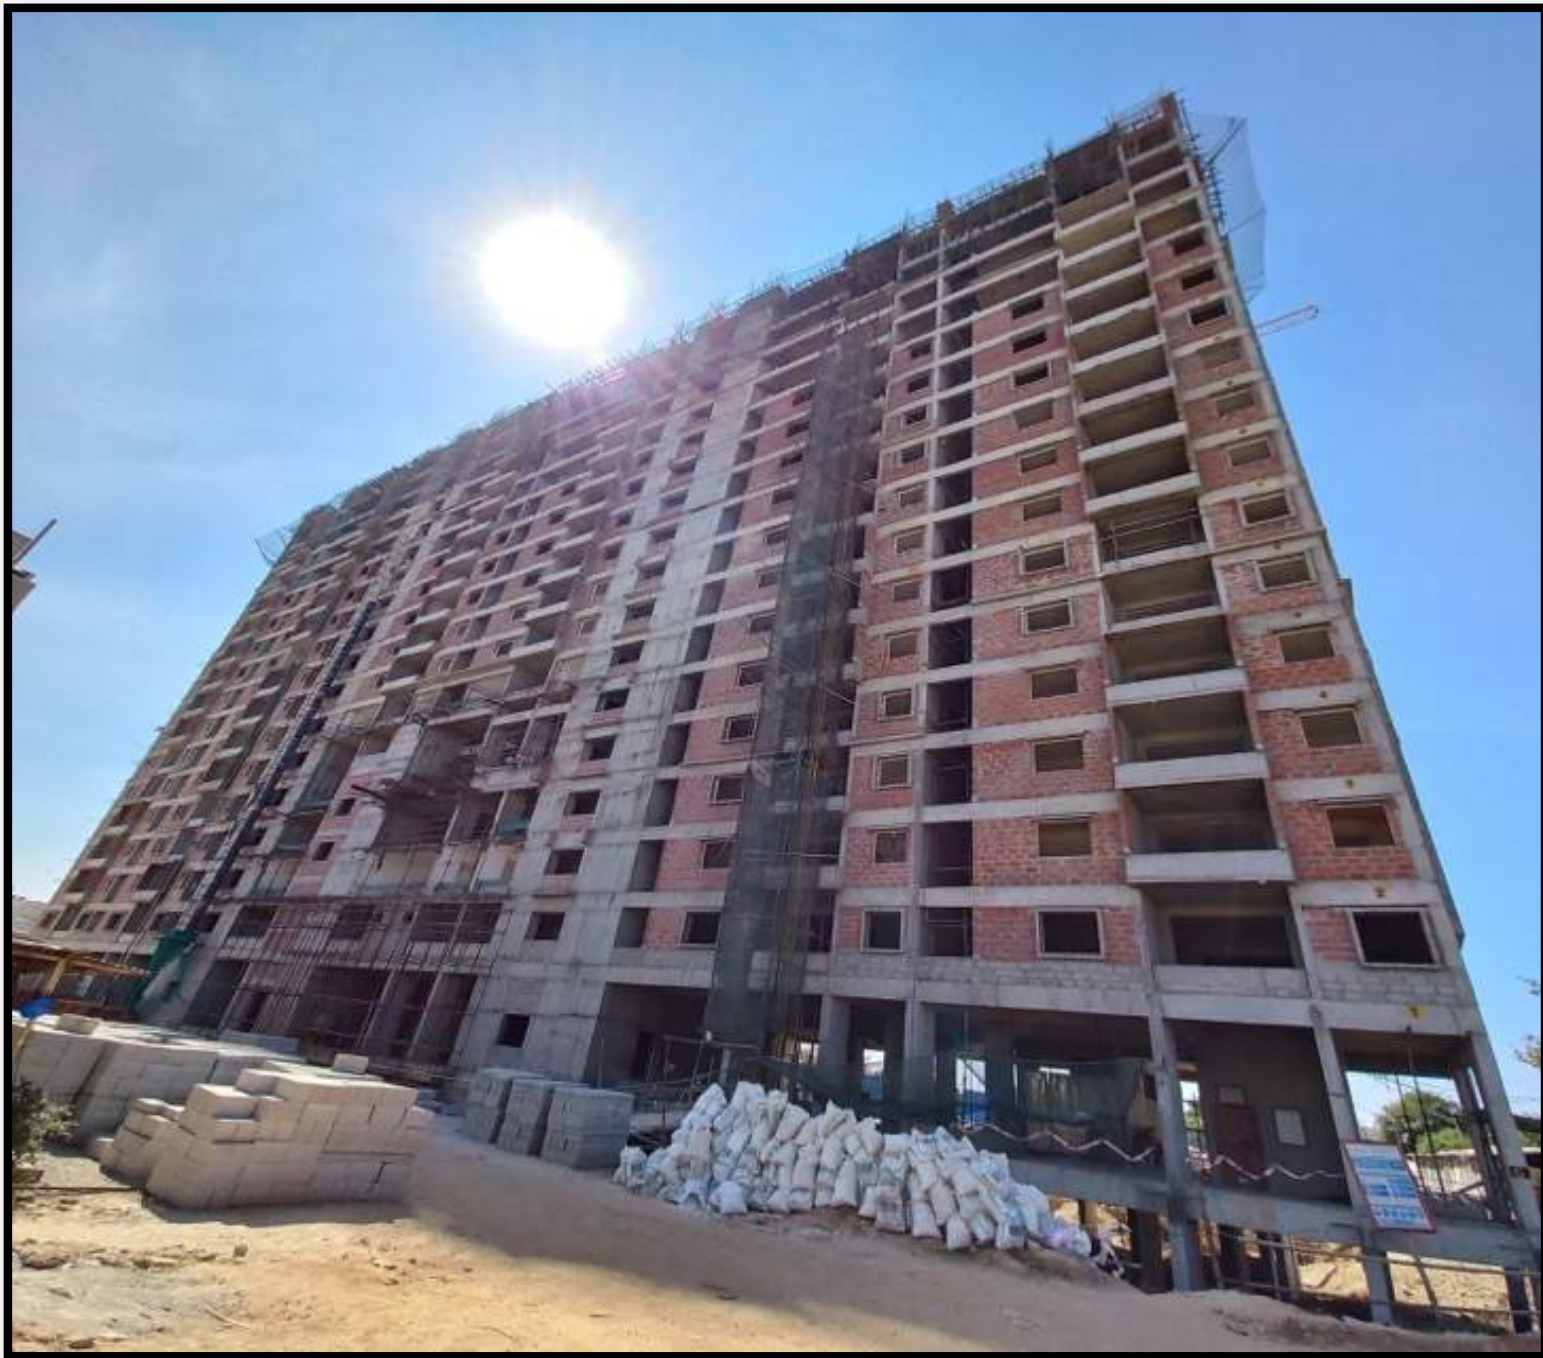

TOWER-01&02 VIEW FROM NORTH EAST FACE



**Tower - I : 18<sup>th</sup> floor slab reinforcement works are in progress.**





**Tower- 2 :18<sup>th</sup> floor shuttering works are in progress.**



**Tower-1 & 2 – Up to 11th floor Block masonry works are completed.**



**Tower-I – 12<sup>th</sup> floor Block masonry works are in progress.**



**Tower-1&2 – Up to 7<sup>th</sup> floor Internal plastering works are completed.**



**Tower-1 & 2- 7<sup>th</sup> floor Internal plastering works are completed.**



**Tower 1 & 2 – 8<sup>th</sup> & 9<sup>th</sup> floor Internal plastering works are in progress**



**Tower 1 & 2 – External plastering works are in progress.**



**Tower 1 & 2 – External plastering works are in progress.**





**Tower-1 & 2 – 10<sup>th</sup> & 11<sup>th</sup> floor electrical wall conduiting & GI box fixing works are in progress.**



[www.habitatventures.com](http://www.habitatventures.com)

# Thank You

#StaySafe #StayPositive #StayHealthy

## Habitat Aura

PRM/KA/RERA/1251/310/PR/181219/002235  
Visit <https://rera.karnataka.gov.in> for further details.
