

Project Progress Status Update as on June 2022

Habitat Aura

PRM/KA/RERA/1251/310/PR/181219/002235 Visit https://rera.karnataka.gov.in for further details.

AT SY. NOs. 49/1, 49/2 & 50 &52/3, AREKERE VILLAGE BEGUR HOBLI, BANGALORE SOUTH TALUK

WORK STATUS

KEY ACTIVITIES

Structure Works:

- > Tower-I(South)
- Up to 10th Floor slab concreting 100% completed and 11th floor Steel bar bending work in progress.
- West side Pour-01 podium slab concrete completed.
- Up to 4th floor block masonry works are 100% completed.
- Fifth & Sixth floor block masonry works are in progress.
- Ground Floor and First floor plastering works are completed.
- Second floor Internal plastering works are in progress.

> Tower-II (North)

- Up to 10th Floor slab concreting 100% completed and 11th floor shuttering work in progress.
- Second & 3rd floor block masonry works are completed and 4th floor in progress.
- Ground Floor plastering works are completed.
- First Floor and Second floor internal plastering works are in progress.





Electrical Works:


> Tower-I(South)

- First floor and Second floor electrical wall conduiting and GI box fixing works are completed.
- Third floor electrical wall conduiting and GI box fixing works are in progress.

• Tower-II (North)

- First floor and Second floor electrical wall conduiting and GI box fixing works are completed.
- Third floor electrical wall conduiting and GI box fixing works are in progress.

TOWER-01&02 VIEW FROM WEST FACE

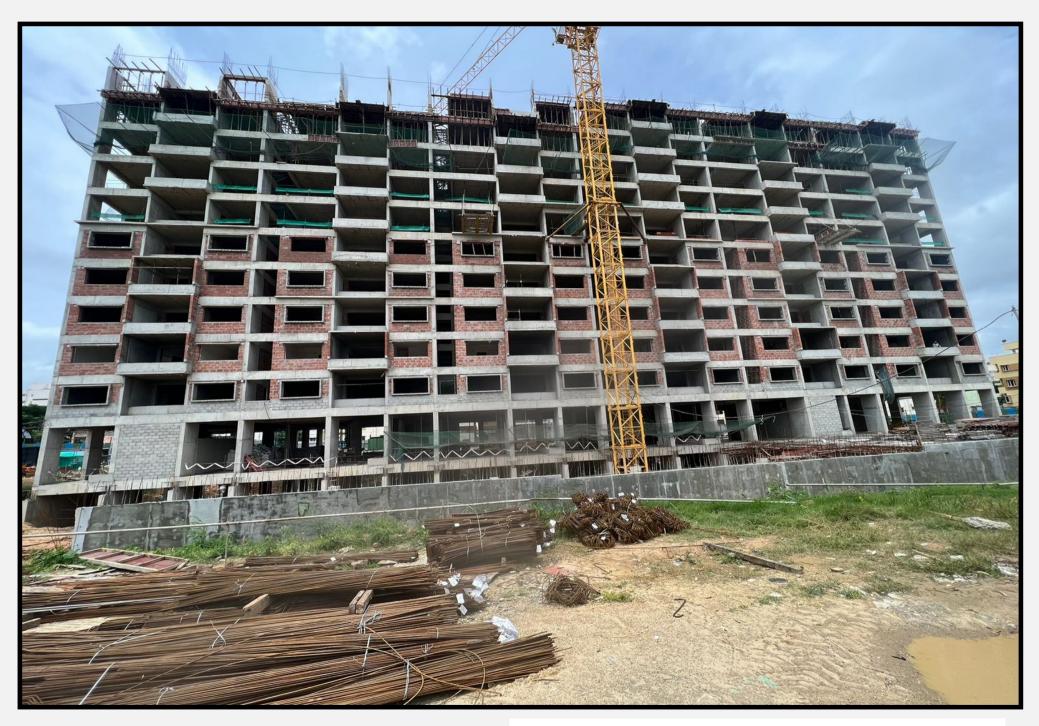

TOWER-01&02 VIEW FROM SW FACE





TOWER-01&02VIEW FROM NORTH EAST FACE



TOWER-01 AERIAL VIEW



TOWER-02 AERIAL VIEW



Block masonry works.



Block masonry works



Block masonry works











Electrical wall conduiting & GI box fixing works



electrical wall conduiting & GI box fixing works



www.habitatventures.com

Thank You

#StaySafe #StayPositive #StayHealthy #GetVaccine #BreaktheChain

Habitat Aura

PRM/KA/RERA/1251/310/PR/181219/002235 Visit https://rera.karnataka.gov.in for further details.
